



WHY ARE WE STUDYING PROJECT MANAGEMENT AT FANSHAWE?

- Because only 26% of projects in the working world today are successfully delivered respecting the triple constraint.



DEFINITIONS



Project management is the discipline of organizing and managing resources using a carefully defined set of activities to meet the pre-defined objectives of the client.

The management of a "**project**" versus a "**process**" is often very different and requires varying technical skills and philosophy, hence requiring the development of project management.



WHAT IS:

✖ a Project?

A project is a **temporary** and **one-time** endeavor.

A project is a sequence of unique, complex, and connected activities having one goal or purpose and it must be completed by a specific time, within budget, and according to defined specification.

✖ a Process?

A process is a **permanent endeavor**, designed to be repetitive, undertaken to create a unique product or service, which brings about beneficial change or added value.



Why are projects important?

- Projects help companies overcome these challenges:
 - 1. Shortened product **life cycles**
 - 2. Narrow product launch windows
 - 3. Increasingly **complex** and technical products
 - 4. Emergence of **global markets**
 - 5. An economic period marked by low inflation



PRIMARY AND SECONDARY CHALLENGE OF PROJECT MANAGEMENT

The **primary challenge** of project management is to make sure that a project is **delivered** within **defined constraints**.

The **second**, more ambitious challenge is the **optimized** allocation and integration of **resources** needed to meet pre-defined objectives.



PROJECT MANAGEMENT GOVERNING BODIES

The **Project Management Institute** (*PMI*), incorporated in 1969, was founded by five volunteers, with its headquarters in Newtown Square, outside Philadelphia, Pennsylvania. It has published several standards related to project management and manages several levels of project management certification.

The standard *Project Management Body of Knowledge (PMBOK)* guide, currently in its seventh edition, is the only ANSI standard for project management.

There is presently no ISO project management standard, but the **International Project Management Association** in co-ordination with PMI is in the process of writing one.

As of November 2021, the PMI serves more than 2.0 million professionals including over 650,000 members in 213 countries and territories around the world, with 313 chapters and 14,000 volunteers serving local members in over 80 countries.



PROJECT CONSTRAINTS

Projects are limited by items called **constraints**

- **Cost** – mostly labor cost, but also hardware, software, training, etc.
- **Time** (*schedule*)
- **Scope** (*Requirements/objectives*)
- **Resources** – people (*skills*), facilities, equipment, etc.
- In reality we can only control and manage at most, two of these constraints
- Which constraints can your project tolerate flexibility in?



THE TRIPLE CONSTRAINT



Scope

Time: available to complete the project

Cost: budgeted amount of money to complete the project

Scope: what must be done to complete a project's end result

Quality: Stakeholder **Satisfaction** and Quality of Product/Service

Quality

Cost

Time




THE 5 MAIN PHASES IN A PROJECT

1. Initiating
 2. Planning
 3. Executing
 4. Controlling
 5. Closing
- } Often simultaneous



PROJECT MANAGEMENT PROCESS LIFE CYCLE

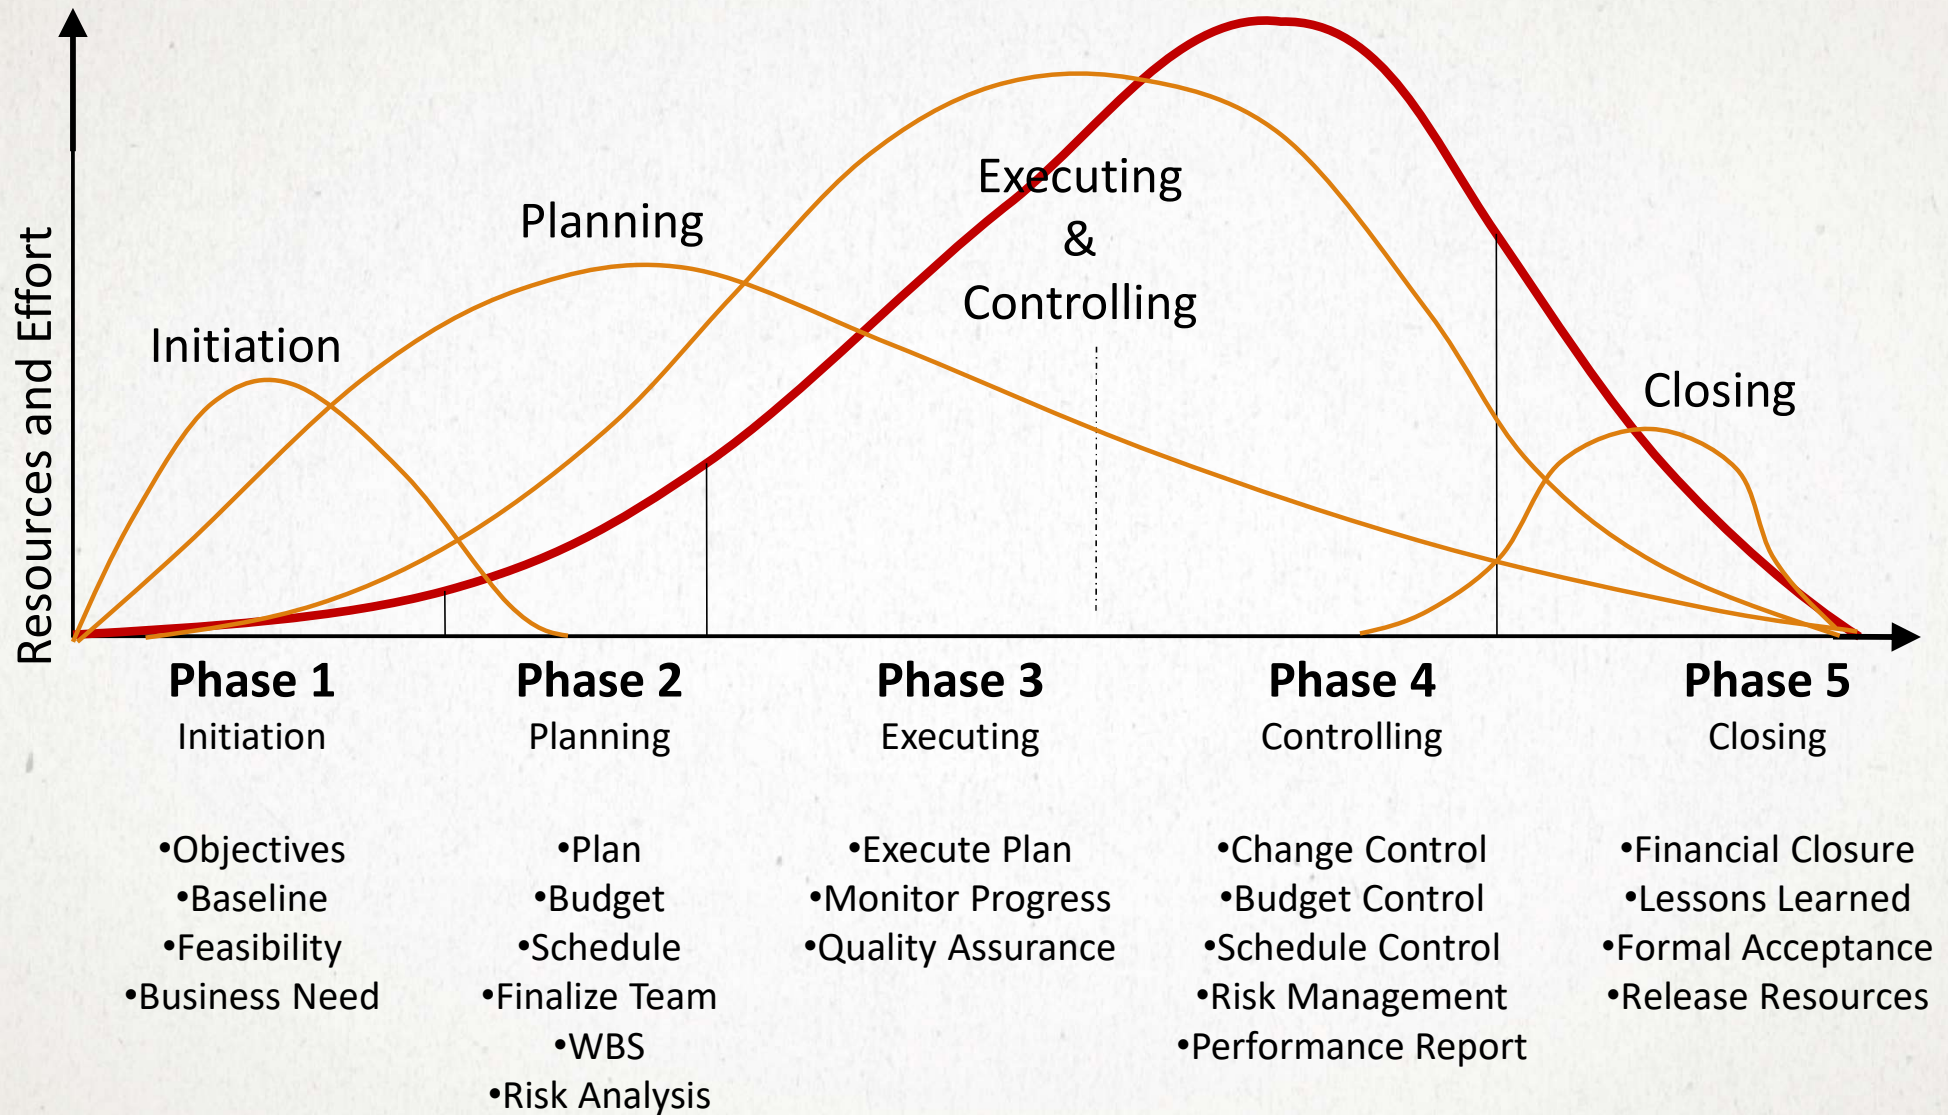

INITIATING THE PROJECT

To begin this process, you must first understand **what** it is you are **trying to do** and **why you should do it**.

1. You must **define** the business case for the project. Does it fit within your Project Portfolio?
2. Are there **Project Sponsors** available and who are they?
3. Create the **Project Charter** and obtain sign off from all the involved parties.



PLANNING THE PROJECT

- This is the stage that determines the ultimate success or failure of your project. It is here that the largest amount of work is done to prepare the tools that will be used for the actual management of the project.
1. Create the **Scope Statement**
 2. Create the **Work Breakdown Structure (WBS)**
 3. Create the **Network Diagram (AON)**
 4. Create the **Budget**
 5. Create the **Risk Assessment** and **Mitigation Plans**
 6. Determine Quality Standards
 7. Create the **Project Control System**
 8. Create the **Communication Protocols**



EXECUTION

- This is where the **Project Manager** transitions from being an **active participant** in the process to being more of an **observer** of the process.
- **Control** must be maintained to ensure that all tasks are being completed on time, on budget and meeting all quality requirements.
- The Project Manager must be able to focus on the details and see the big picture at the same time. Leadership qualities are most important during this phase of the project.
- This is where you lead your team and **manage the project**.



CONTROLLING

- All the **Control Processes** put in place during the planning phase are now put to the test.
- Scope control, change management, schedule control become **daily review items**.
- This phase of the project overlaps the **Execution** phase and are sometimes grouped as one phase in some textbooks.



CLOSING

- This is where the final reviews of budget, schedule and scope are completed. **Customer sign off** is obtained and resources are returned to their home departments.
 - This is the most difficult phase to complete effectively and has the most impact on future projects.
1. Create **final project report**
 2. Conduct **lessons learned**
 3. Obtain final payments and provide final payments for any contracted services.



THE HIERARCHY OF CONSIDERATION FOR IMPORTANT DECISION MAKING FOR PROJECT MANAGERS

1. Safety
2. What is best for the company I represent?
3. What is best for the Project sponsor?
4. What is best for the customer?
5. What is best for the suppliers?



CODE OF ETHICS FOR PROJECT MANAGERS

- **Ethics** (*definition*) – "That branch of philosophy dealing with values relating to **human conduct**, with respect to the rightness and wrongness of certain actions and to the goodness and badness of the motives and ends of such actions.
- So, you can violate ethics without breaking laws – that is the implication. But like all rules that are broken, there are consequences.
- In this case, if you were an **accredited project manager**, a viable career choice for you, you would have to swear to uphold the **Project Management Institute Code of Ethics**. Were you to break the code, you would place yourself in conflict with your profession and risk losing your position in business. Violating it severely enough could have legal ramifications.



PMI CODE OF ETHICS – KEY ASPECTS

- The code is to be adhered to by all PMI members, PMI applicants, and PMI volunteers. College students studying the art of project management and its materials are not bound to this code of ethics.
- The **guiding principle** of the document is: "As practitioners of project management, we are bound to do what is right and honorable."
- The code consists of both aspirational, and mandatory standards of behavior.
- **RESPONSIBILITY, RESPECT, FAIRNESS, AND HONESTY** are the 4 pillars of the project management code of ethics.



PROJECT COMMUNICATIONS

All the process that are required to ensure timely and appropriate communication of project information.
These **processes** include:

- 1) Plan Communications Management
- 2) Manage Communications
- 3) Control Communications



WHAT DO WE COMMUNICATE?

- 1) Project plans
- 2) Project meetings
- 3) Status updates
- 4) Organization charts
- 5) Requirements – what are we doing?
- 6) Contracts
- 7) Presentations
- 8) Policies and procedures



HOW DO WE COMMUNICATE

- Talking:
 - one on one,
 - meetings,
 - presentations,
 - phone
- Written:
 - emails,
 - reports
- Paralanguage – the tone we use
- Body language
- Other
- Our actions?




PERFORMANCE REPORTING

- Typical **performance reports** include:
 - 1) Status report (*where the project now stands*)
 - 2) Progress report (*what has been accomplished*)
 - 3) Trend report (*examining project reports over time to see if performance is **improving** or **deteriorating***)
 - 4) Forecasting report (***predicting** future project status and performance*)
 - 5) Variance report (*comparing **actual results** to **planned***)
 - 6) Earned Value (*integrating scope, cost and schedule measures to assess project performance*)



HOW OFTEN WE COMMUNICATE

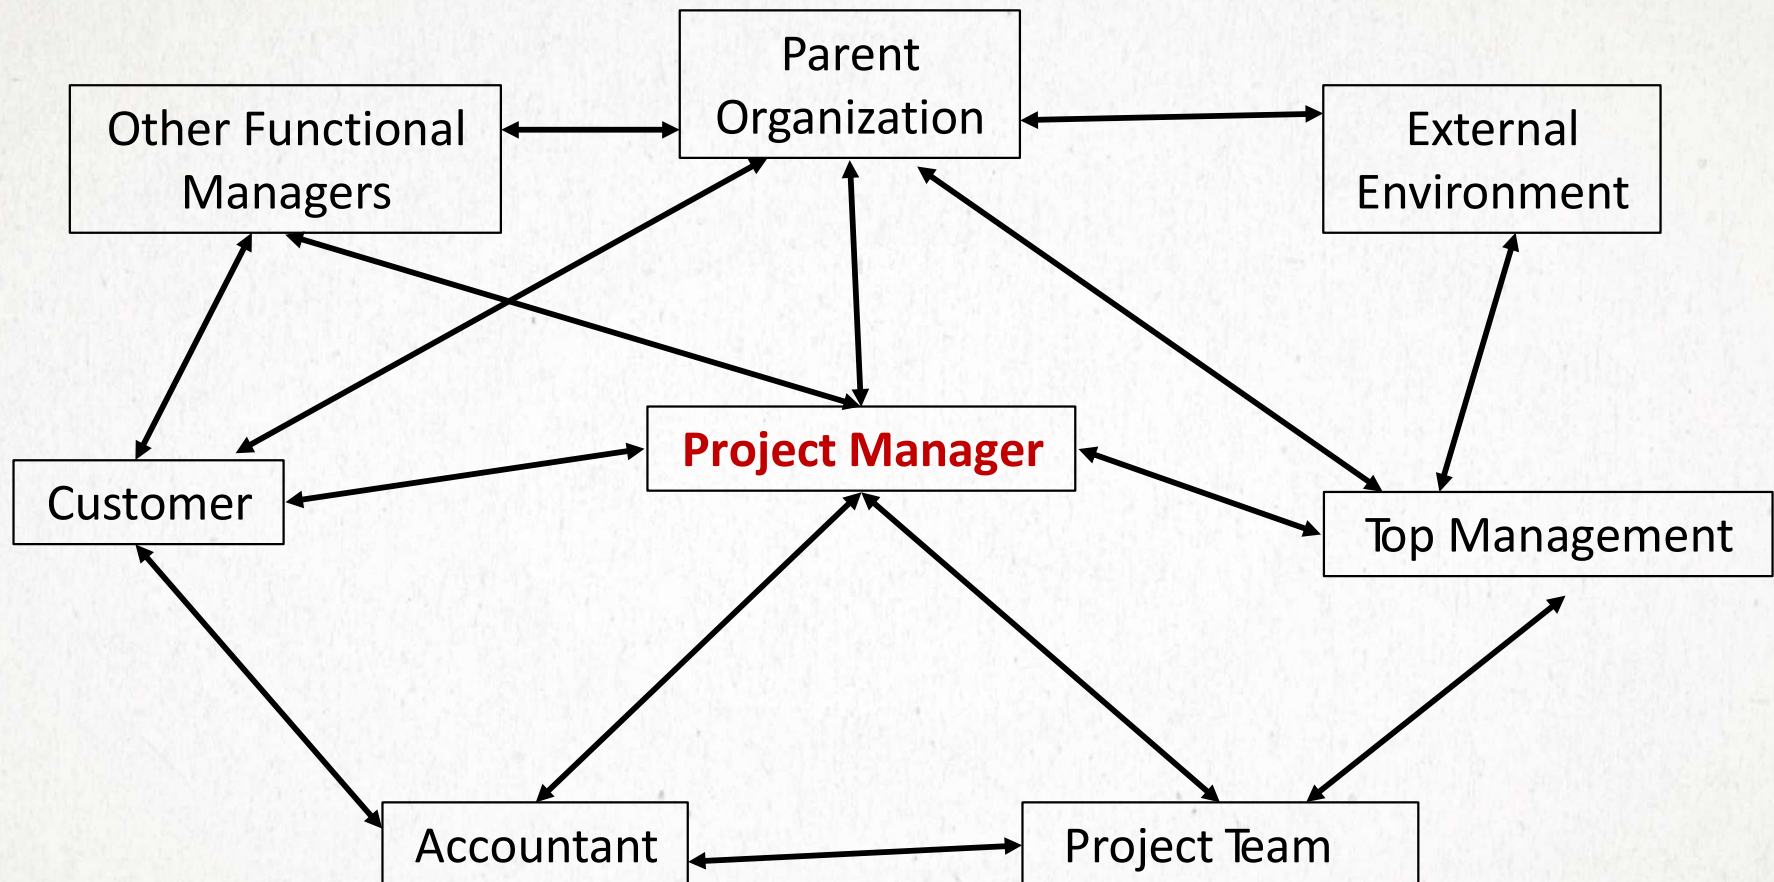

n = number of people communicating

$$\# \text{ interactions} = \frac{n(n-1)}{2}$$

PROJECT COMMUNICATIONS MANAGEMENT

The **process** of developing an appropriate approach and plan for **project communication** based on your stakeholder's information needs and requirements.

Typical elements of the written plan are:

- What information needs to be collected and when
- Who will receive the information
- Methods used to gather and store information
- Limits, if any, on who may give information to whom
- Reporting relationships
- Listing of contact information for all stakeholders
- Schedule for distribution of each type of communication


90% of a Project Manager's time is spent communicating.

MANAGE COMMUNICATIONS

- The **process** of creating, collecting, distributing, etc. of **project information** in accordance with the “**Plan Communications Management**” plan.



COMMUNICATION MODEL

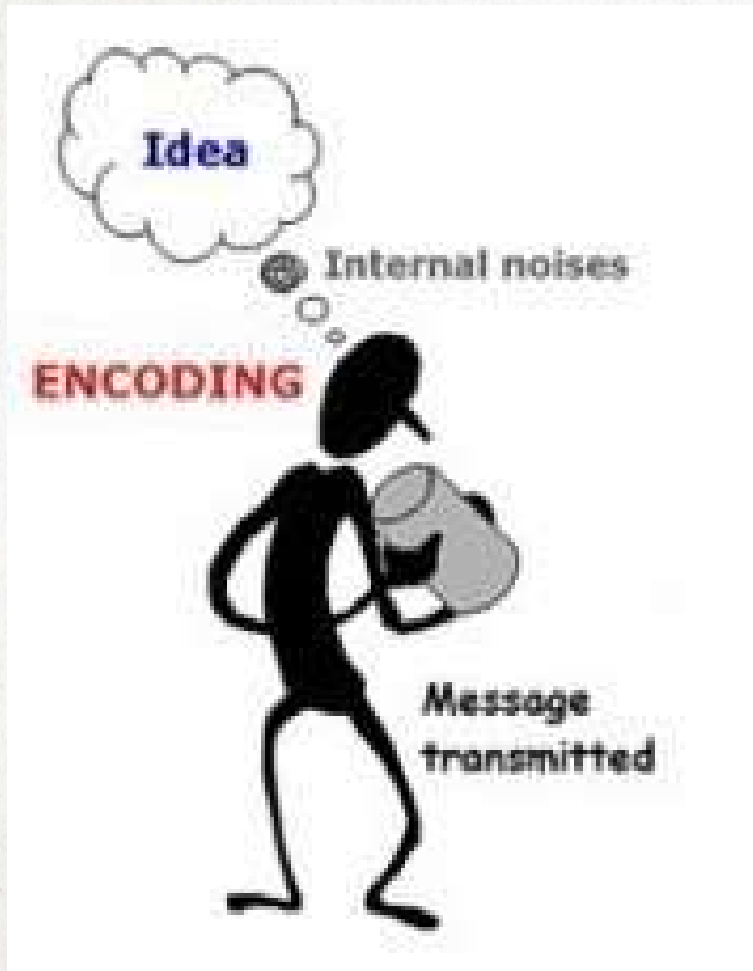

To ensure good project communications, the sender should **encode** a message carefully based upon the

- receiver's education,
- experience,
- language,
- and culture.

The sender should determine the ideal communications method and confirm that the message is understood.




COMMUNICATION MODEL

The receiver should **decode** the message carefully and ensure that the message is **understood**.



THREE ELEMENTS OF COMMUNICATION

- ✗ There are three elements to all communications. There is the **sender**, the **receiver**, and the **message**.

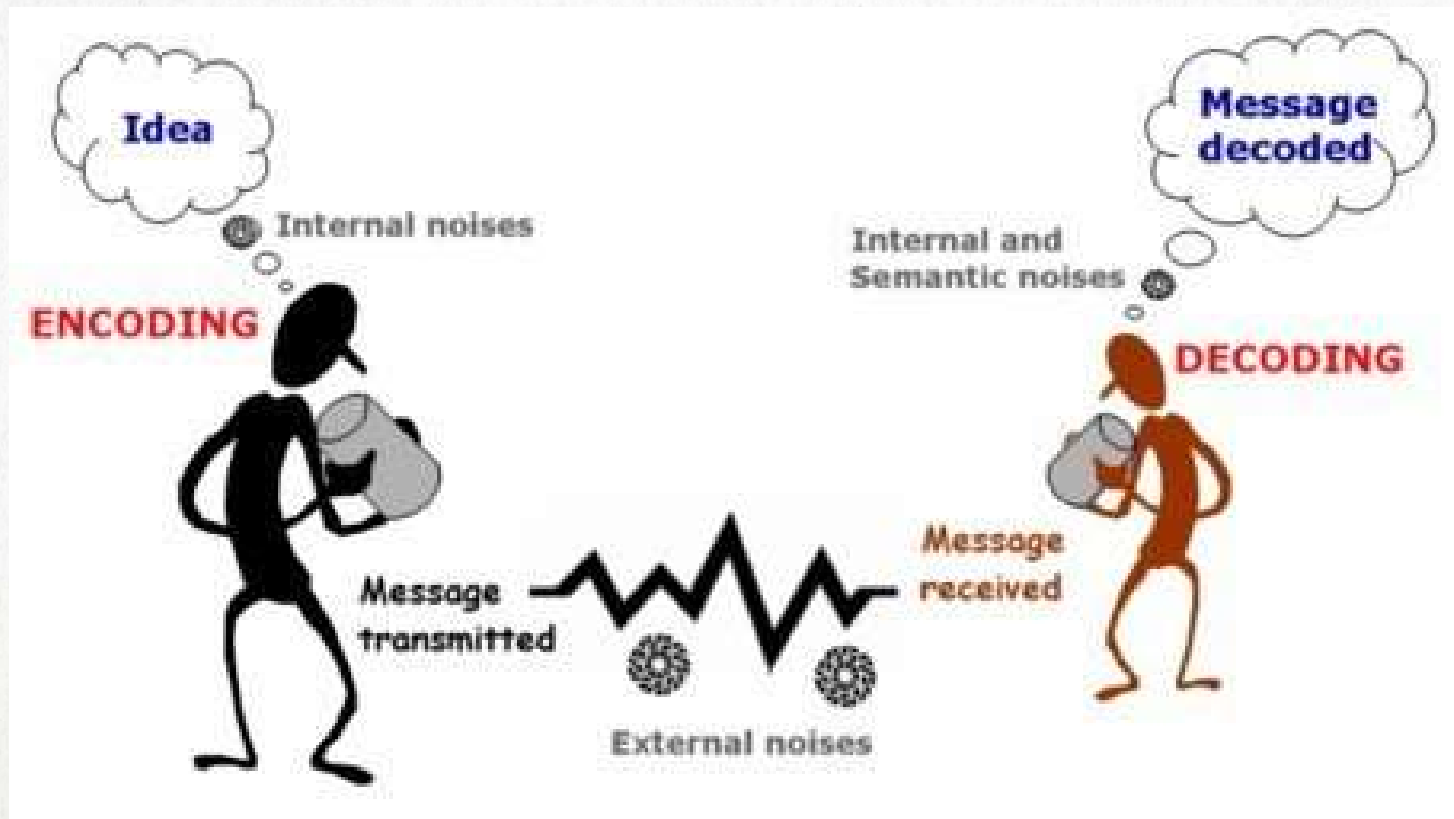

FOUR MODES OF COMMUNICATION

1.	Speaking	23 %	
2.	Reading	13%	
3.	Listening	55%	Scientifically least understood
4.	Writing	9%	



COMMUNICATION CONCEPTS

Nonverbal – about 93% of all person to person communications are non-verbal.

Body Language 55%

Tone of voice 38%, changes to 86% on the phone

- **Active Listening** – The receiver confirms that he/she is listening by agreeing and/or asking for clarification.
- **Effective Listening** – Watching the speaker to pick up physical gestures and facial expressions, thinking about what you say before responding, asking questions, repeating and providing feedback.
- **Feedback** – Saying things like, "Do you understand what I have explained?" usually asked by the sender. Nodding, facial expression of the receiver.



LISTENING FILTERS

- Selective Attention, we decide **what** to focus on.
- Selective Interpretation, we place our own **meaning** on what the person is saying
- Selective Retention, we decide **whether to keep** pieces of information and for how long



SELECTIVE ATTENTION

- ✗ People listen at 500 Words per minute
- ✗ People speak at 150 Words per minute
- ✗ That leaves 350 words per minute to TUNE OUT which represents *(42 seconds)*

- ✗ Causes for TUNING OUT?
 - ☐ Receiver purpose is different from sender's purpose
 - ☐ Under stimulation
 - ☐ Over stimulation (*hot button*)
 - ☐ Pace and delivery



WII-FM

What's In It For Me?

Everything anyone says to you must go through your antenna and be processed through your WII-FM.
If there is something in it for you, you will continue to **pay attention** and **listen**
If not, you are at least partially mentally gone.



SELECTIVE INTERPRETATION

- Gender Patterns
- Generational Patterns
- Geographic Patterns
- Cultural Patterns
- Educational Patterns
- Occupational Patterns



LISTENING DE-RAILERS

Listening without Focus:

Multitasking of your mind, listening to someone while **thinking about something else**.

Listening without Respect: Impatience

Deciding that what the other person is **going to say will be wrong**, so you interrupt and tell them what they should think. They assume a direction the conversation is going, tune out and then respond with what they *thought* was said.

Listening without Respect: Too much ego

Failing to listen to the message of another from *within* **their context** and perspective rather **only from yours**. This is a huge loss in opportunities!

Listening with Bias: Defensive

Developing your response to what you are hearing **while the other person is still talking to you**.

Extremely bad is adverse listening. You listen with a focus to pick out points of difference so you can negate the perception of another.



TIPS TO IMPROVE LISTENING SKILLS

Act like a Listener

Listen to Understand

Stop talking

Give your complete attention

Look at the other person

Empathize (*put yourself in the other's shoes*)

Make understanding your goal

Ask questions

Remain neutral

Take notes

Analyze nonverbal signals and feelings

Hold your rebuttal

Listen to answers given in response

Gain verbal agreement to decisions and action plans

It is important not only to understand, but to check for understanding

realize that listening is hard work

Practice regularly (*come to my classes!*)

Remember that everyone is unique



COMMUNICATION METHODS

When you should use what.....

Formal Written is used when relating complex problems, project plans, project charters, or communicating over long distances.

Formal Verbal is used for presentations and speeches.

Informal Written is used to express memos, e-mails (*careful, e-mails are also contracts*), texts, and other notes.

Informal Verbal is a style best reserved for meetings and conversations.



CONTROL OF COMMUNICATIONS

- Should a Project Manager try to control all communications **between team members** and **outside** of the team?

- **Yes!**

- **Can** a Project Manager control all communications?

- **No!**

