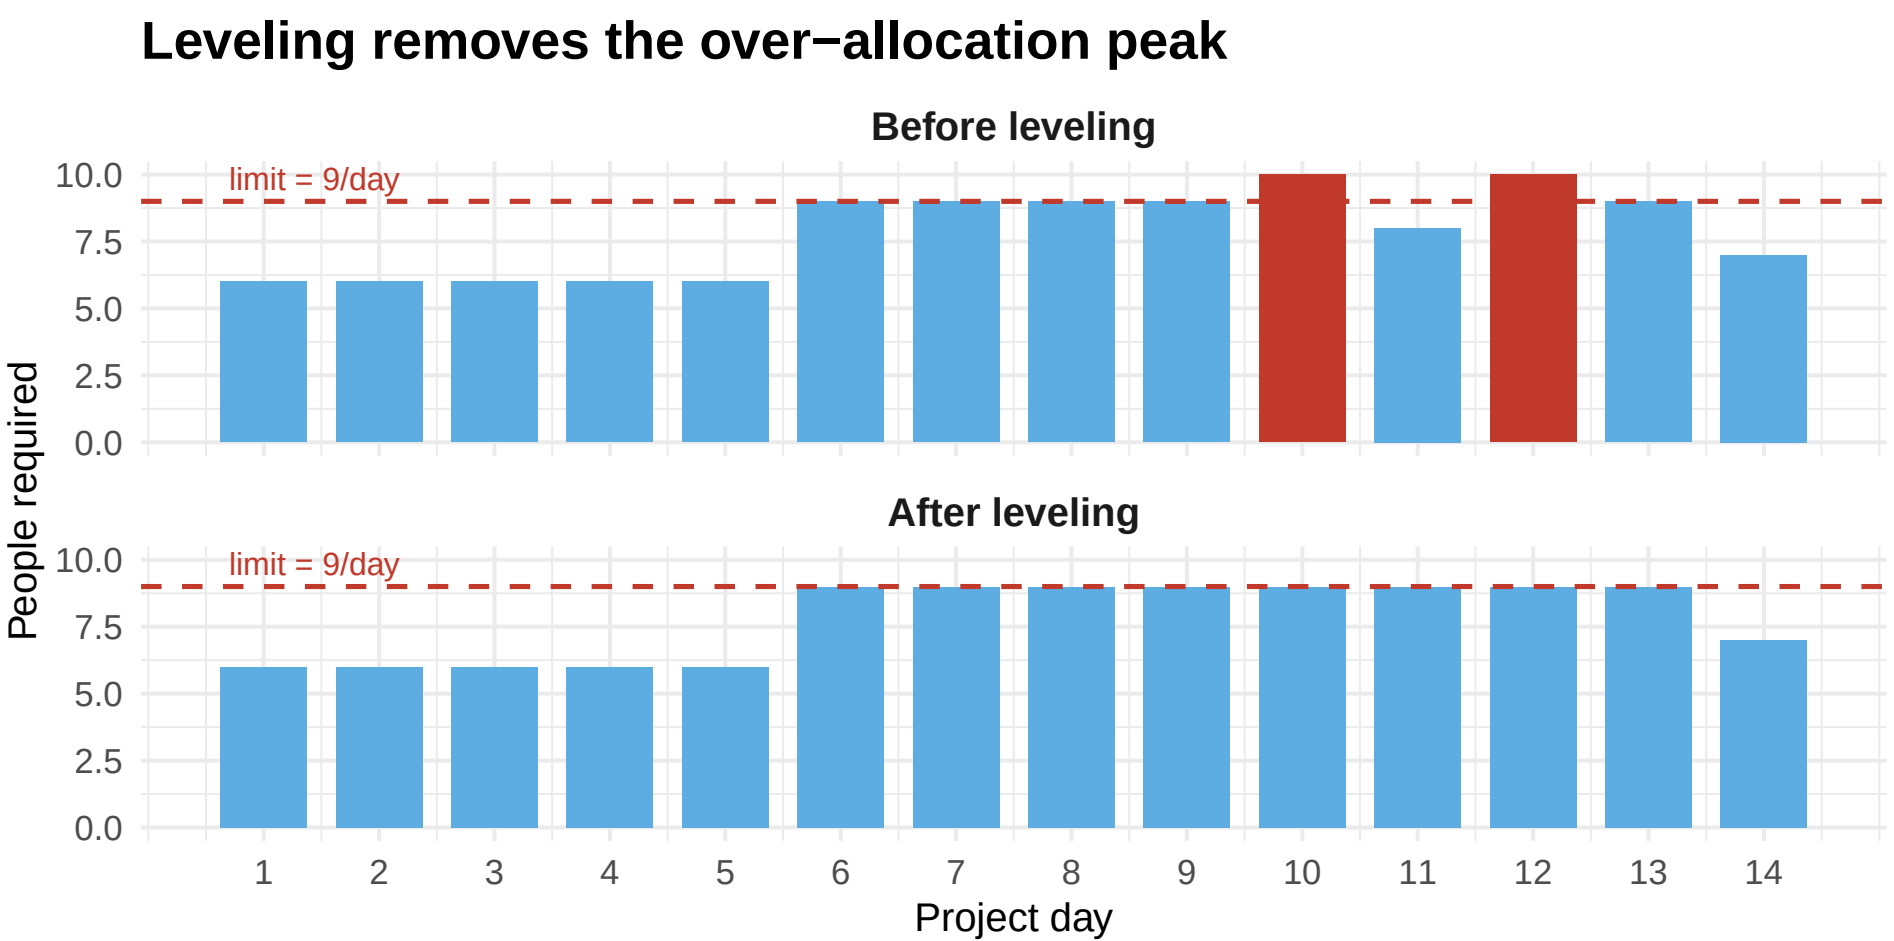
Leveling removes the over−allocation peak
Before leveling
limit = 9/day
10.0
7.5
5.0
2.5
0.0
After leveling
limit = 9/day
10.0
7.5
5.0
2.5
0.0
People required
1
2
3
4
5
6
7
8
9
10
11
12
13
14
Project day
